


North Hampton Library Addition & Renovation

ID	Task Mode	Task Name	Duration	Start	Finish
1		Pre-Construction Effort	138 days?	Mon 3/25/19	Wed 10/2/19
2		Schematic Design	28 days?	Mon 3/25/19	Wed 5/1/19
3		Schematic Design Budget Check	15 days	Thu 5/2/19	Wed 5/22/19
4		Budget Correction (if required)	5 days	Thu 5/23/19	Wed 5/29/19
5		Design Development	43 days	Thu 5/2/19	Mon 7/1/19
6		Design Development Budget Check	15 days	Tue 7/2/19	Mon 7/22/19
7		Design Development Budget Correction (if required)	5 days	Tue 7/23/19	Mon 7/29/19
8		Construction Documents	45 days	Tue 7/2/19	Mon 9/2/19
9		Bid Period	15 days	Tue 9/3/19	Mon 9/23/19
10		Prepare Guaranteed	20 days	Thu 9/5/19	Wed 10/2/19
11		Construction Period	215 days	Thu 10/3/19	Wed 7/29/20
12		Mobilize Site for Construction	3 days	Thu 10/3/19	Mon 10/7/19
13		Implement Site Safety & Logistics	4 days	Thu 10/3/19	Tue 10/8/19
14		Excavate for Concrete Footings	3 days	Wed 10/9/19	Fri 10/11/19
15		Concrete Foundation	23 days	Mon 10/14/19	Wed 11/13/19
16		Structure & Building Envelope	48 days	Thu 11/14/19	Mon 1/20/20
17		Pour Slab on Grade	4 days	Tue 1/14/20	Fri 1/17/20
18		Roofing	10 days	Tue 1/21/20	Mon 2/3/20
19		Mechanical & Electrical Rough - In	25 days	Tue 2/4/20	Mon 3/9/20
20		Interior Finishes	42 days	Tue 3/3/20	Wed 4/29/20
21		Mechanical & Electrical Finish	5 days	Thu 4/30/20	Wed 5/6/20
22		Punchlist	5 days	Thu 5/7/20	Wed 5/13/20
23		Occupancy of New Additon	0 days	Wed 5/13/20	Wed 5/13/20
24		Phased Renovation	55 days	Thu 5/14/20	Wed 7/29/20
25		Final Entry Infill Addition	25 days	Thu 5/28/20	Wed 7/1/20
26		Completion & Occupancy	0 days	Wed 7/29/20	Wed 7/29/20

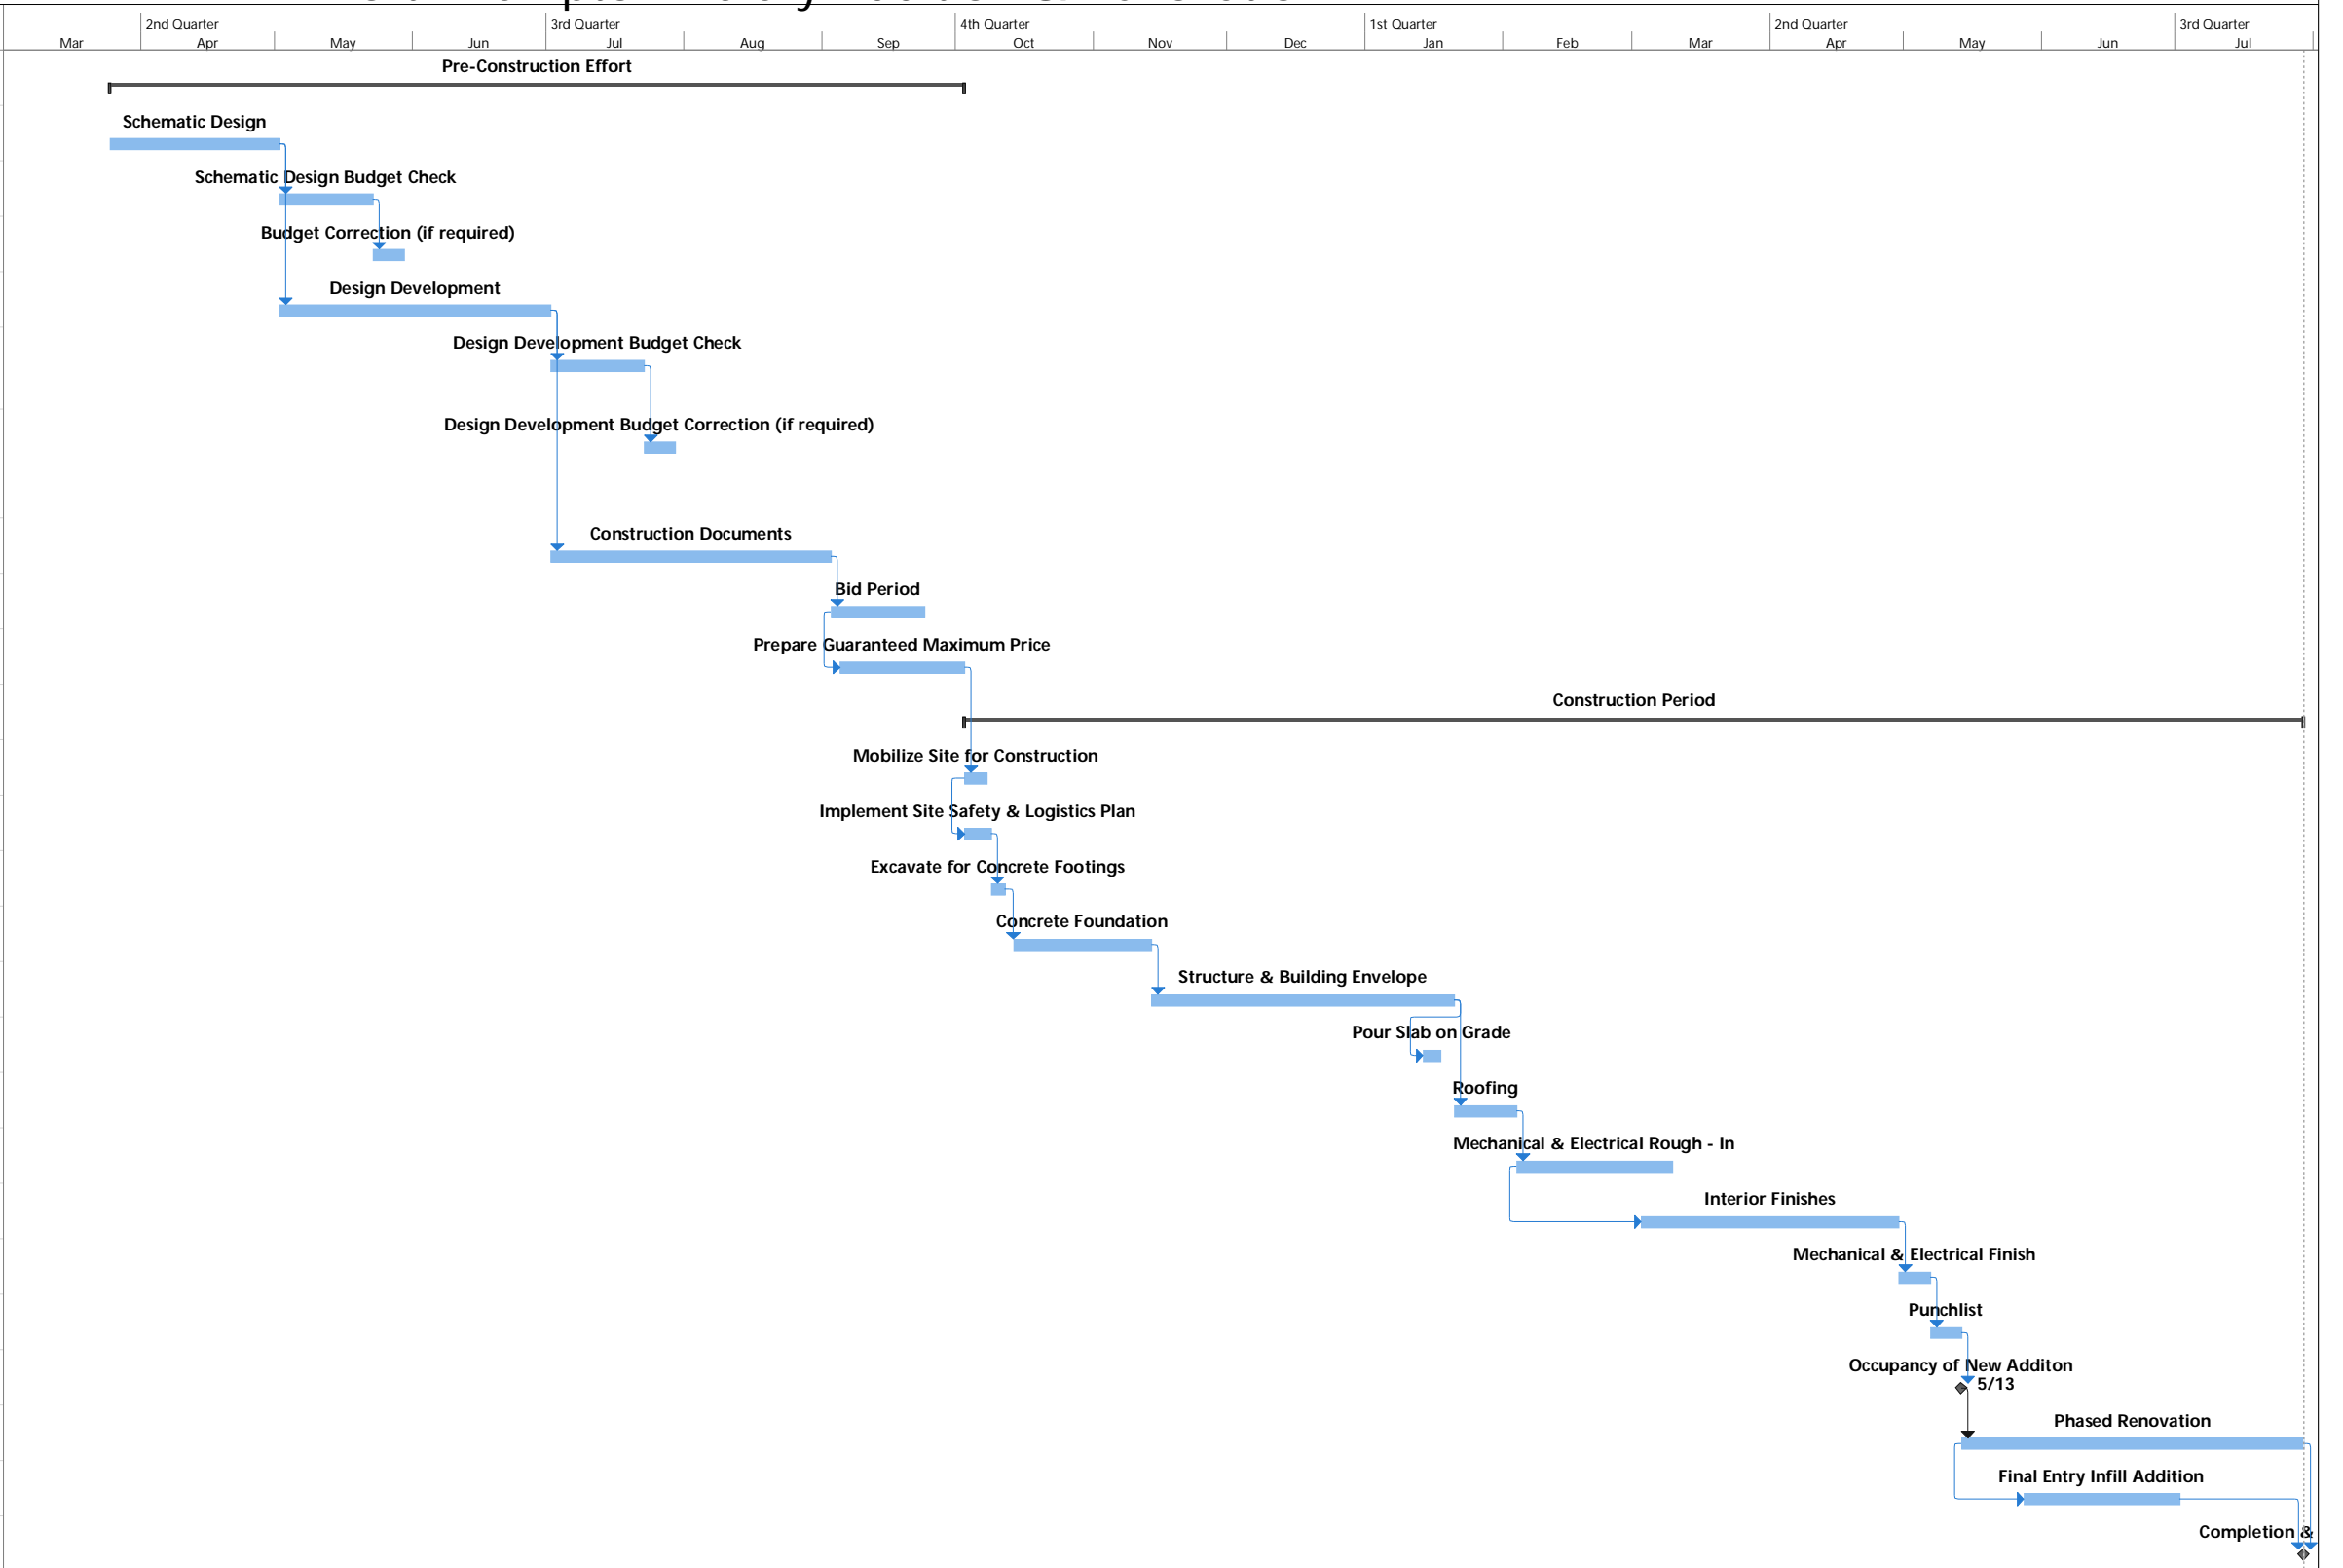

Project: North hampton Library

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			
